

PROGRESS OF CONSTRUCTION WORK

1. New parking lot has been completed and is being utilized by the school.
2. New accessible main entrance ramp & stairs have been completed and are being utilized by the school.
3. Loadbearing masonry and pre-cast slab installation has been completed.
4. All masonry works have been completed.
5. Concrete floor slabs for both wings have been completed.
6. Above ceiling mechanical & electrical rough ins in both wings have been completed.
7. Above ceiling mechanical & electrical in the gym wing is approximately 95% complete.
8. Roofing works on both additions are approximately 95% complete and cap flashings are being installed.
9. Exterior façade (vapour barrier/insulation/brick/metal cladding) works are approximately 95% complete.
10. Window installations are completed.
11. New hydro services works are completed, and the school is now on permanent power.
12. Rooftop mechanical equipment has been installed.
13. Interior finishes work is approximately 90% completed. This includes VCT & tile flooring, painting, suspended ceilings, lighting fixtures, plumbing fixtures, and millwork.
14. Works including new tile flooring (ground floor), new ceiling grid, new lighting & emergency lighting in the existing building have been completed.
15. Exterior improvement works to the extended pick-up/drop-off, playfield and playground have commenced.
16. Renovated washrooms in the existing building are approximately 95% complete. New staff washroom on the second floor is in use.
17. Structural works converting the existing gym into new kindergarten rooms have been completed.
18. Elevator installation is approximately 80% complete.

UPCOMING WORK

1. Mechanical & Electrical rough-in works in the new Kindergarten rooms will continue.
2. Gym equipment installation and stage drapery will continue.
3. New polyurethane gym flooring is scheduled to commence mid-October.
4. Commissioning of mechanical & electrical systems will commence in the next couple of weeks.
5. Fire alarm testing and verifications are commencing.

Hollywood Public School Project Update

October 11, 2024


COMMUNITY UPDATE:

The added works to modernize the existing building with updated lighting, ceilings, ground floor porcelain tile and emergency lighting have significantly improved the appearance of the interiors as well as safety within the school (see pictures & descriptions below).

During the summer the General Contractor took over the existing gym to allow for mechanical and life safety tie-ins of the new additions to the existing building. These works had to be undertaken as the life safety components were required to be operational so occupancy could be granted for the new gym. At that time, it was anticipated that the new gym would be turned over to the school for use in mid-September. Unfortunately, due to supply chain issues, beyond the control of the contractor or TDSB, the delivery of ducting and equipment for the new gym were delayed and the September handover could not be achieved. The current anticipated handover for the new gym is anticipated for mid-November 2024.

The overall project is progressing well and remains on track for completion towards the end of 2024.

CONSTRUCTION PROGRESS PHOTOS:

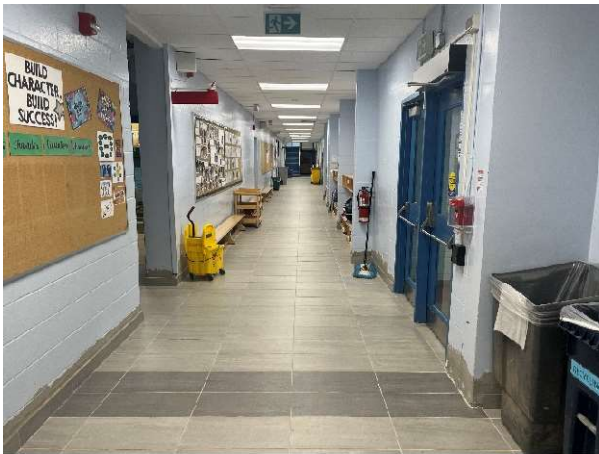

Interior photo of new tiling, ceiling grid, lighting, and emergency lighting in ground floor corridor.



Interior photo of new ceiling grid, lighting and emergency lighting in ground floor corridor.



Interior photo of new staff washroom on second floor.



Interior photo of new universal barrier free washroom under construction on ground floor.

Hollywood Public School Project Update

October 11, 2024



Interior photo of new classroom facing west currently under construction. Flooring, whiteboards/tac boards and millwork have been installed and room is ready for above ceiling inspections.



Interior photo of new classroom facing southeast currently under construction. Flooring, whiteboards/tac boards and millwork have been installed and room is ready for above ceiling inspections.



Interior photo looking to the east for the new of the new girls' washroom currently under construction on the second floor of the new addition.




Interior photo looking to the east for the new of the new boys' washroom currently under construction on the second floor of the new addition.

Hollywood Public School Project Update

October 11, 2024



Interior picture of new elevator being installed in childcare/classroom wing.

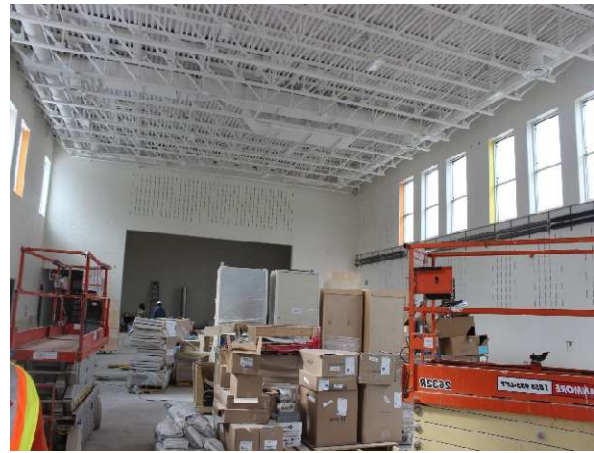

Interior photo looking east in the new gym towards the stage.



Exterior photo of the east elevation of the new gym addition showing completed brick, metal panels, metal siding and windows.



Exterior photo of the north elevation of the new childcare/classroom addition showing completed brick, metal panels, metal siding and windows.
